

## TECHNICAL MEMORANDUM

---

**To:** David Gibson, San Diego Regional Water Quality Control Board      **Date:** February 28, 2014

**From:** Chris Osuch, Adam Gale, and Elizabeth Appy, Anchor QEA      **Project:** 131003-01.02

**Cc:** Michael Chee, National Steel and Shipbuilding Company  
Michael Palmer, de maximis, inc.  
David Templeton and Michael Whelan, Anchor QEA  
Robert Smith, U.S. Army Corps of Engineers

**Re:** San Diego Shipyard Sediment Site – South Shipyard (Place ID 794466, Order No. R9-2013-0093) Weekly Water Column Monitoring Report: February 17 to 22, 2014

---

### INTRODUCTION

The San Diego Bay Environmental Restoration Fund – South (South Trust) is remediating contaminated sediments at the South Shipyard portion of the San Diego Shipyard Sediment Site (Site). Remediation is required to comply with Cleanup and Abatement Order (CAO) No. R9-2012-0024 issued by the San Diego Regional Water Quality Control Board (Water Board 2012a). Water column monitoring must be conducted during dredging or sand placement operations in order to comply with the Waste Discharge Requirements and Section 401 Water Quality Certification (WDR/WQC; Water Board 2013). Anchor QEA was contracted by the South Trust to conduct this water column monitoring.

Weekly monitoring reports are required in accordance with Mitigation Measure (MM) 4.2.4 of the Mitigation Monitoring and Reporting Program (MMRP; Water Board 2012b) and Appendix C of the Remedial Action Plan (Anchor QEA 2012). This technical memorandum summarizes results of water column monitoring between February 17 and 22, 2014. During this week, monitoring was conducted on February 17. Water quality monitoring included dissolved oxygen (DO), pH, turbidity, and visual observations.

---

## WATER QUALITY MONITORING RESULTS

DO, pH, and turbidity were measured 10 feet below the surface at each station using a Hydrolab MS5 multi-probe sonde. Monitoring was performed at the reference station, two early warning stations, and four compliance stations. The reference station is located 1,000 feet from the remedial footprint in the direction of the ocean (Figure 1). Early warning and compliance stations are located 250 and 500 feet from the construction area, respectively. The general layout of early warning and compliance monitoring locations for Sediment Management Unit (SMU)-4 are shown on Figure 2; however, actual locations were positioned in the field relative to the construction area.<sup>1</sup>

A summary of monitoring results during sand placement is presented in Table 1. Compliance criteria were not exceeded. No visual evidence of discoloration, turbidity, or surface pollution was observed. The double silt curtain was in place, and no damage, dislocation, or gaps were observed during the monitoring.

## REFERENCES

- Anchor QEA, 2012. *Remedial Action Plan*. San Diego Shipyard Sediment Site. Revised October 2012.
- Water Board (San Diego Regional Water Quality Control Board), 2012a. Cleanup and Abatement Order R9-2012-0024 for the Shipyard Sediment Site. Issued March 14, 2012.
- Water Board, 2012b. Mitigation Monitoring and Reporting Program for the Shipyard Sediment Remediation Project Environmental Impact Report (SCH#2009111098). Issued on March 14, 2012.
- Water Board, 2013. Waste Discharge Requirements for San Diego Shipyard Sediment Remediation Project, San Diego Bay, San Diego, California. Order No. R9-2013-0093. Issued on July 10, 2013.

---

<sup>1</sup> The construction area is defined as the area occupied by the dredging barge, sediment scow, sand and rock placement equipment, demolition work equipment, silt curtains, and other work.

---

# TABLE

---

**Table 1**  
**Water Quality Monitoring Results During Material Placement - February 17 through 22, 2014**

Date	Time	Station Type	Station ID	Latitude <sup>1</sup>	Longitude <sup>1</sup>	Water Quality Measurements			Visual Observations		
						DO (mg/L)	pH	Turbidity (NTU)	Odor	Presence of Surface Pollution	Discoloration or Turbidity
2/17/2014	13:43:28	Reference	P-BG-140217	32.69153	-117.15070	8.1	7.9	0.9	No	No	No
2/17/2014	14:07:05	Early Warning	P-EWN-140217	32.68759	-117.14047	7.9	7.9	0.3	No	No	No
2/17/2014	14:19:46	Compliance	P-CNN-140217	32.68956	-117.14041	7.9	7.9	1.0	No	No	No
2/17/2014	14:27:48	Compliance	P-CON-140217	32.68764	-117.14120	7.8	8.0	1.0	No	No	No
2/17/2014	14:32:35	Early Warning	P-EWS-140217	32.68682	-117.13987	7.9	8.0	0.6	No	No	No
2/17/2014	14:36:11	Compliance	P-COS-140217	32.68602	-117.13933	7.9	8.0	0.7	No	No	No
2/17/2014	14:40:24	Compliance	P-CNS-140217	32.68635	-117.13776	8.0	8.0	0.2	No	No	No

Notes:

Receiving water limitation compliance criteria: DO shall not be depressed more than 10 percent from the reference (BG); pH shall not be changed more than 0.2 units from reference (BG); pH shall not be depressed below 7.0 nor raised above 9.0; turbidity must not exceed 20 percent of reference (BG; if natural turbidity from 0 to 50 NTU).

DO = dissolved oxygen

mg/L = milligrams per liter

NTU = Nephelometric Turbidity Units

1 Latitude and longitude coordinates in decimal degrees, North American Datum 1983 (NAD83)

# FIGURES

---


L:\AutoCAD Project Files\Projects\0995-SD Bay Environmental\SD Shipyard\0995-RP-027 REF SAMP 2.dwg FIG 1

Nov 07, 2013 10:04am mpratschner



**SOURCE:** Aerial from ESRI base maps. Upland topography from Digital Mapping Inc., dated September 2009, and supplemented by Environmental Data Solutions survey dated April 13, 2013.  
**HORIZONTAL DATUM:** California State Plane, Zone 6, NAD83, U.S. Feet.


**NOTES:**  
 Reference Sampling Location BG  
 Latitude: 32° 41.4970'  
 Longitude: 117° 09.0185'



L:\AutoCAD Project Files\Projects\0995-SD Bay Environmental\SD Shipyard\0995-RP-023 WQ SAMP.dwg FIG 4 SMU-4

Oct 23, 2013 2:21pm mpratschner

**SOURCE:** Upland topography from Digital Mapping Inc., dated September 2009, and supplemented by Environmental Data Solutions survey dated April 13, 2013.  
**HORIZONTAL DATUM:** California State Plane, Zone 6, NAD83, U.S. Feet.

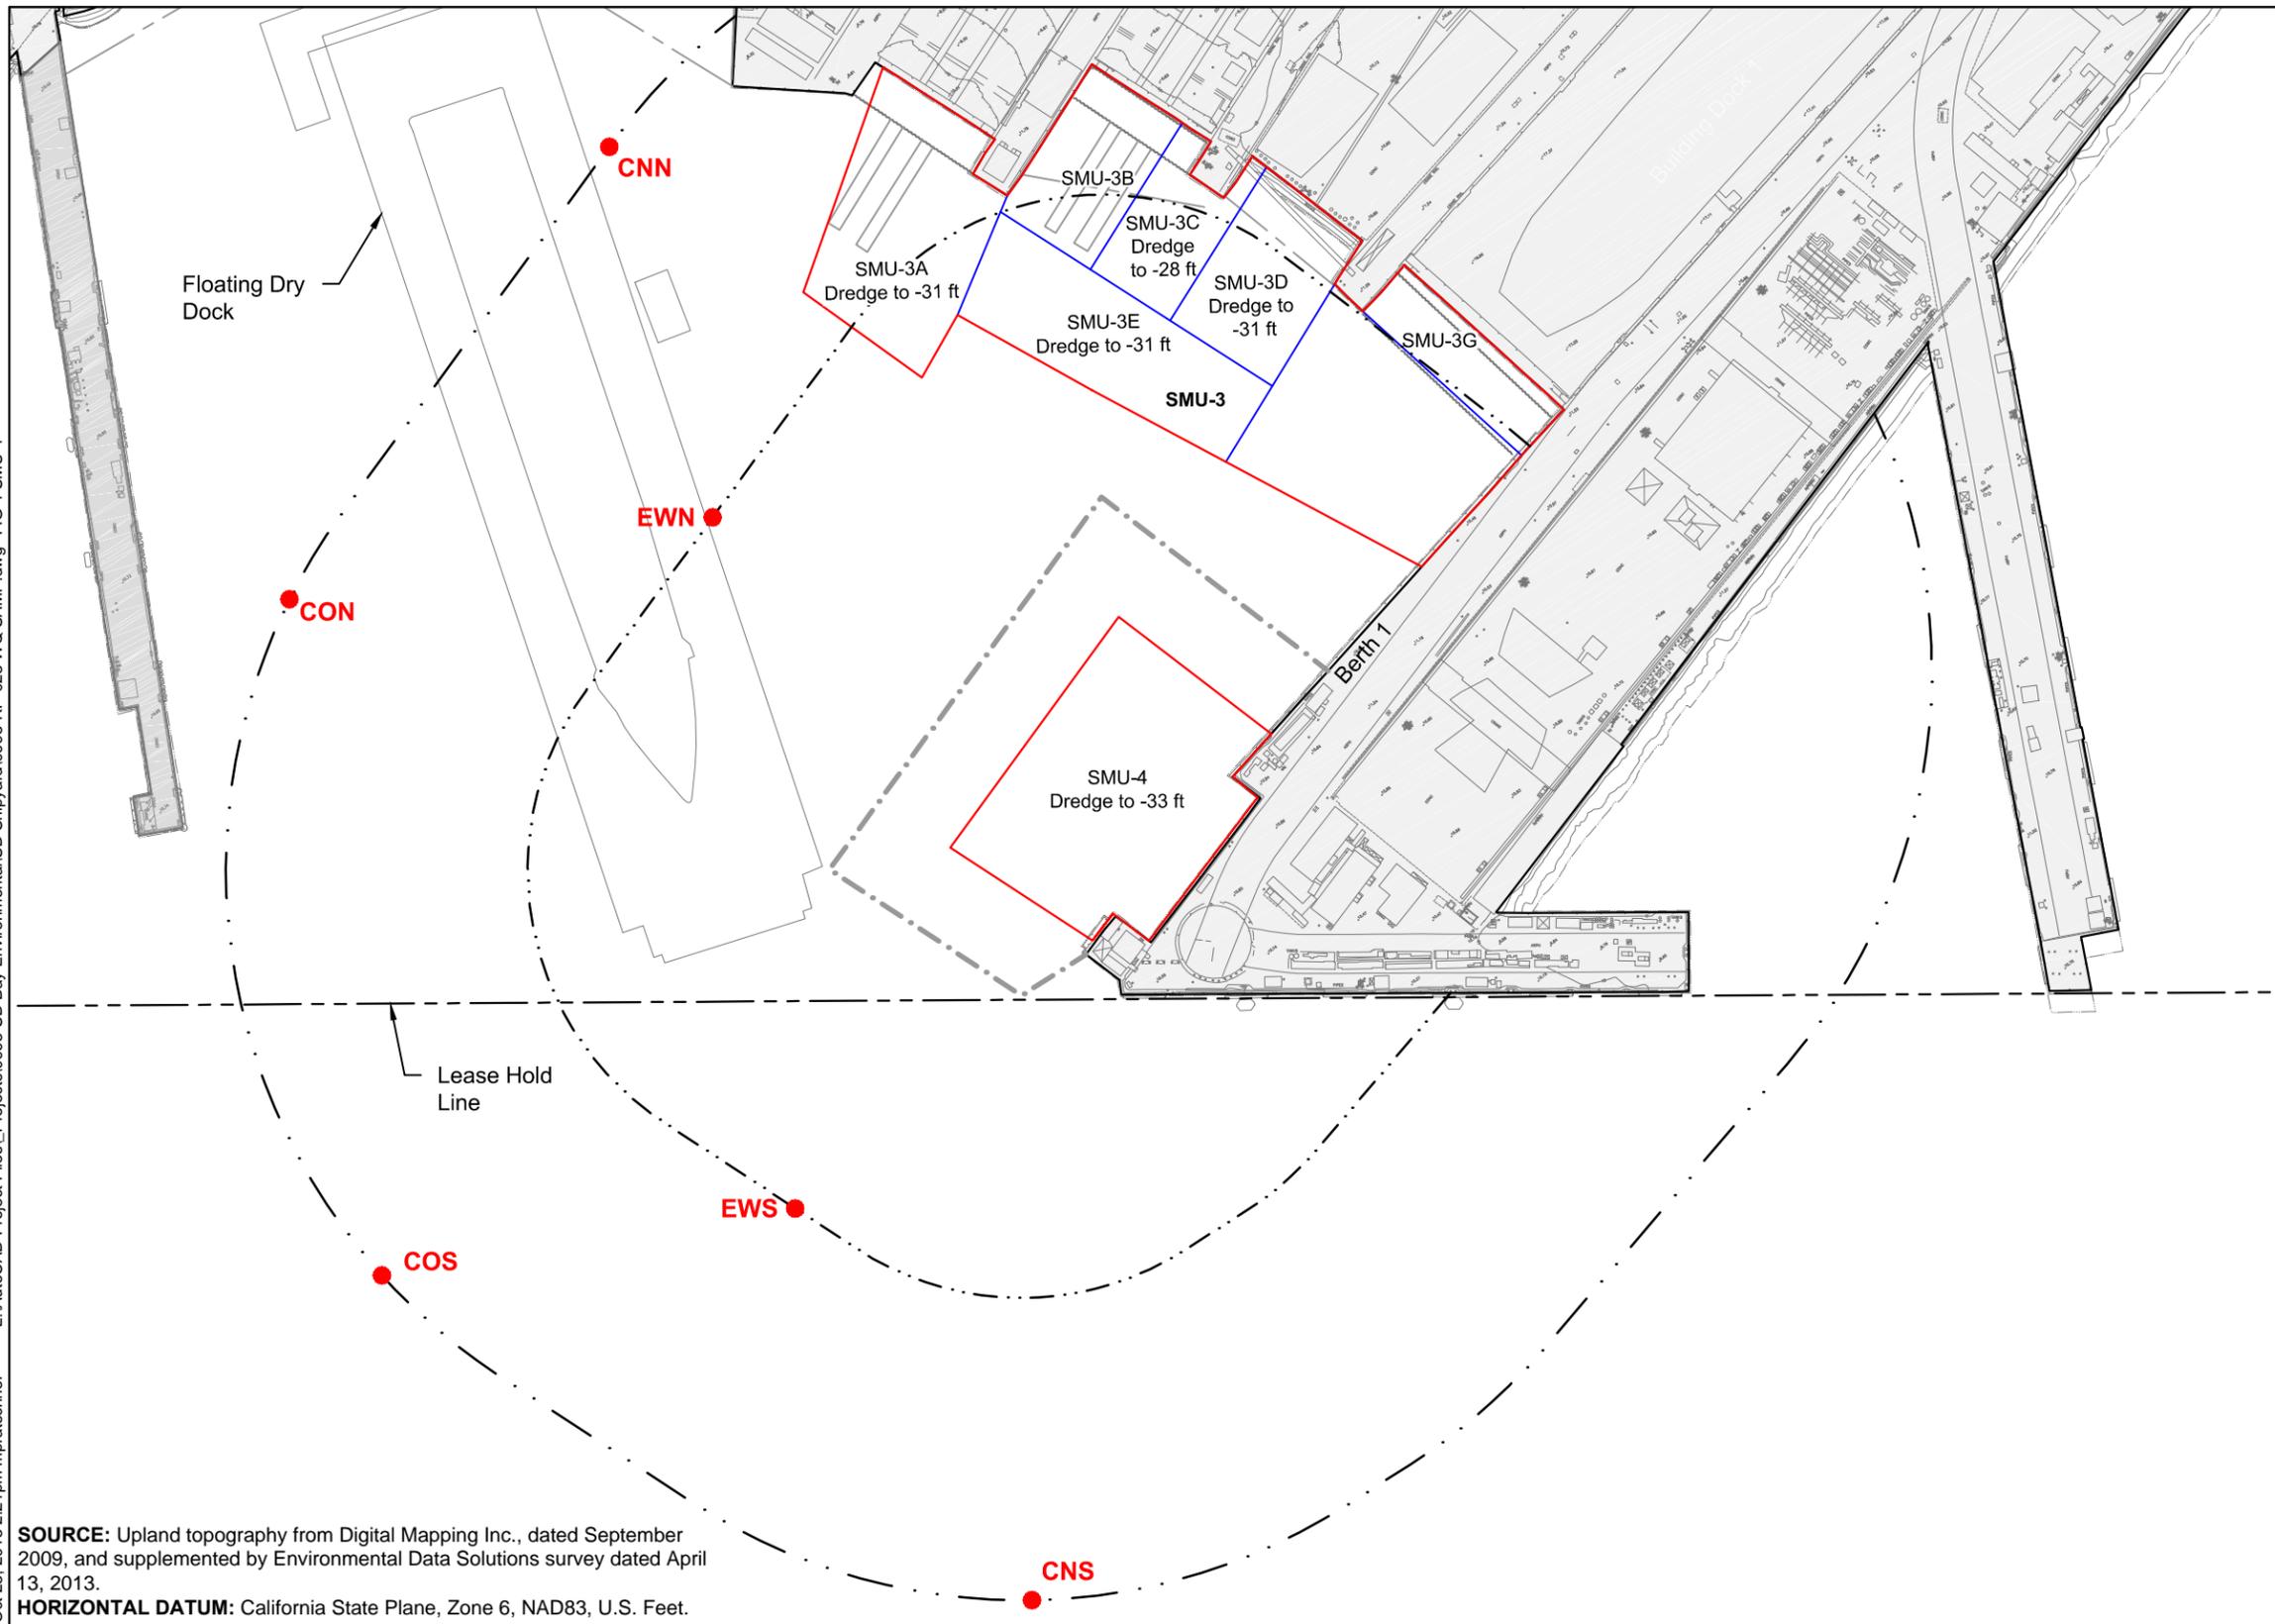

**LEGEND:**

	Remediation Boundary
	Sub-SMU Boundary
	250 ft from Construction Area
	500 ft from Construction Area
	Sampling Location
	Silt Curtain
EWN	Early Warning North
EWS	Early Warning South
CNN	Compliance Nearshore North
CNS	Compliance Nearshore South
CON	Compliance Offshore North
COS	Compliance Offshore South

**NOTE:**  
 Actual sampling locations determined in the field based on the location of the construction area.

