ANCHOR QEA

27201 Puerta Real, Suite 350
Mission Viejo, California 92691
Phone 949.347.2780
www.anchorqea.com

TECHNICAL MEMORANDUM

To:	David Gibson, San Diego Regional Water Quality Control Board	**Date:**	November 12, 2013
From:	Chris Osuch, Adam Gale, and Elizabeth Appy, Anchor QEA	**Project:**	131003-01.02
Cc:	Michael Chee, National Steel and Shipbuilding Company Michael Palmer, de maximis, inc. David Templeton and Michael Whelan, Anchor QEA Robert Smith, U.S. Army Corps of Engineers		
Re:	San Diego Shipyard Sediment Site – South Shipyard (Place ID 794466, Order No. R9-2013-0093) Weekly Water Column Monitoring Report: October 28 to November 2, 2013		

INTRODUCTION

The San Diego Bay Environmental Restoration Fund – South (South Trust) is remediating contaminated sediments at the South Shipyard portion of the San Diego Shipyard Sediment Site (Site). Remediation is required to comply with Cleanup and Abatement Order (CAO) No. R9-2012-0024 issued by the San Diego Regional Water Quality Control Board (Water Board 2012a). Water column monitoring must be conducted during dredging operations in order to comply with the Waste Discharge Requirements and Section 401 Water Quality Certification (WDR/WQC; Water Board 2013). Anchor QEA was contracted by the South Trust to conduct this water column monitoring.

Weekly monitoring reports are required in accordance with Mitigation Measure (MM) 4.2.4 of the Mitigation Monitoring and Reporting Program (MMRP; Water Board 2012b) and Appendix C of the Remedial Action Plan (Anchor QEA 2012). This technical memorandum summarizes results of water column monitoring between October 28 and November 2, 2013. During this week, monitoring was conducted on October 31. Water quality monitoring included dissolved oxygen (DO), pH, turbidity, and visual observations.

WATER QUALITY MONITORING RESULTS

DO, pH, and turbidity were measured 10 feet below the surface at each station using a Hydrolab MS5 multi-probe sonde. Monitoring was performed at the reference station, two early warning stations, and four compliance stations. The reference station is located 1,000 feet from the remedial footprint in the direction of the ocean (Figure 1). Early warning and compliance stations are located 250 and 500 feet from the construction area, respectively. The general layout of early warning and compliance monitoring locations for Sediment Management Unit (SMU)-3 are shown on Figure 2; however, actual locations were positioned in the field relative to the construction area.[1]

A summary of monitoring results during dredging is presented in Table 1. Compliance criteria were not exceeded. No visual evidence of discoloration, turbidity, or surface pollution was observed. The double silt curtain was in place and no damage, dislocation, or gaps were observed.

REFERENCES

Anchor QEA, 2012. *Remedial Action Plan*. San Diego Shipyard Sediment Site. Revised October 2012.

Water Board (San Diego Regional Water Quality Control Board), 2012a. Cleanup and Abatement Order R9-2012-0024 for the Shipyard Sediment Site. Issued March 14, 2012.

Water Board, 2012b. Mitigation Monitoring and Reporting Program for the Shipyard Sediment Remediation Project Environmental Impact Report (SCH#2009111098). Issued on March 14, 2012.

Water Board, 2013. Waste Discharge Requirements for San Diego Shipyard Sediment Remediation Project, San Diego Bay, San Diego, California. Order No. R9-2013-0093. Issued on July 10, 2013.

[1] The construction area is defined as the area occupied by the dredging barge, sediment scow, sand and rock placement equipment, demolition work equipment, silt curtains, and other work.

TABLE

Table 1

Water Quality Monitoring Results During Dredging - October 28 through November 2, 2013

Date	Time	Station Type	Station ID	Latitude[1]	Longitude[1]	Water Quality Measurements			Visual Observations		
						DO (mg/L)	pH	Turbidity (NTU)	Odor	Presence of Surface Pollution	Discoloration or Turbidity
10/31/2013	12:40:12	Reference	D-BG-131031	32.69172	-117.15057	7.1	7.9	2.9	No	No	No
10/31/2013	13:06:55	Early Warning	D-EWN-131031	32.68978	-117.13920	6.8	7.9	1.1	No	No	No
10/31/2013	13:17:31	Early Warning	D-EWS-131031	32.68740	-117.13937	6.6	7.9	2.0	No	No	No
10/31/2013	13:22:12	Compliance	D-CNN-131031	32.68964	-117.14029	6.7	7.9	1.9	No	No	No
10/31/2013	13:26:12	Compliance	D-CON-131031	32.68779	-117.14066	6.7	7.9	1.9	No	No	No
10/31/2013	13:30:36	Compliance	D-CNS-131031	32.68643	-117.13951	6.7	8.0	1.9	No	No	No
10/31/2013	13:39:40	Compliance	D-COS-131031	32.68663	-117.14044	7.0	8.0	1.8	No	No	No

Notes:

Receiving water limitation compliance criteria: DO shall not be depressed more than 10 percent from the reference (BG); pH shall not be changed more than 0.2 unit from reference (BG); pH shall not be depressed below 7.0 nor raised above 9.0; turbidity must not exceed 20 percent of reference (BG; if natural turbidity from 0 to 50 NTU).

DO = dissolved oxygen

mg/L = milligrams per liter

NTU = Nephelometric Turbidity Units

1 Latitide and longitude coordinates in decimal degrees, North American Datum 1983 (NAD83)

FIGURES

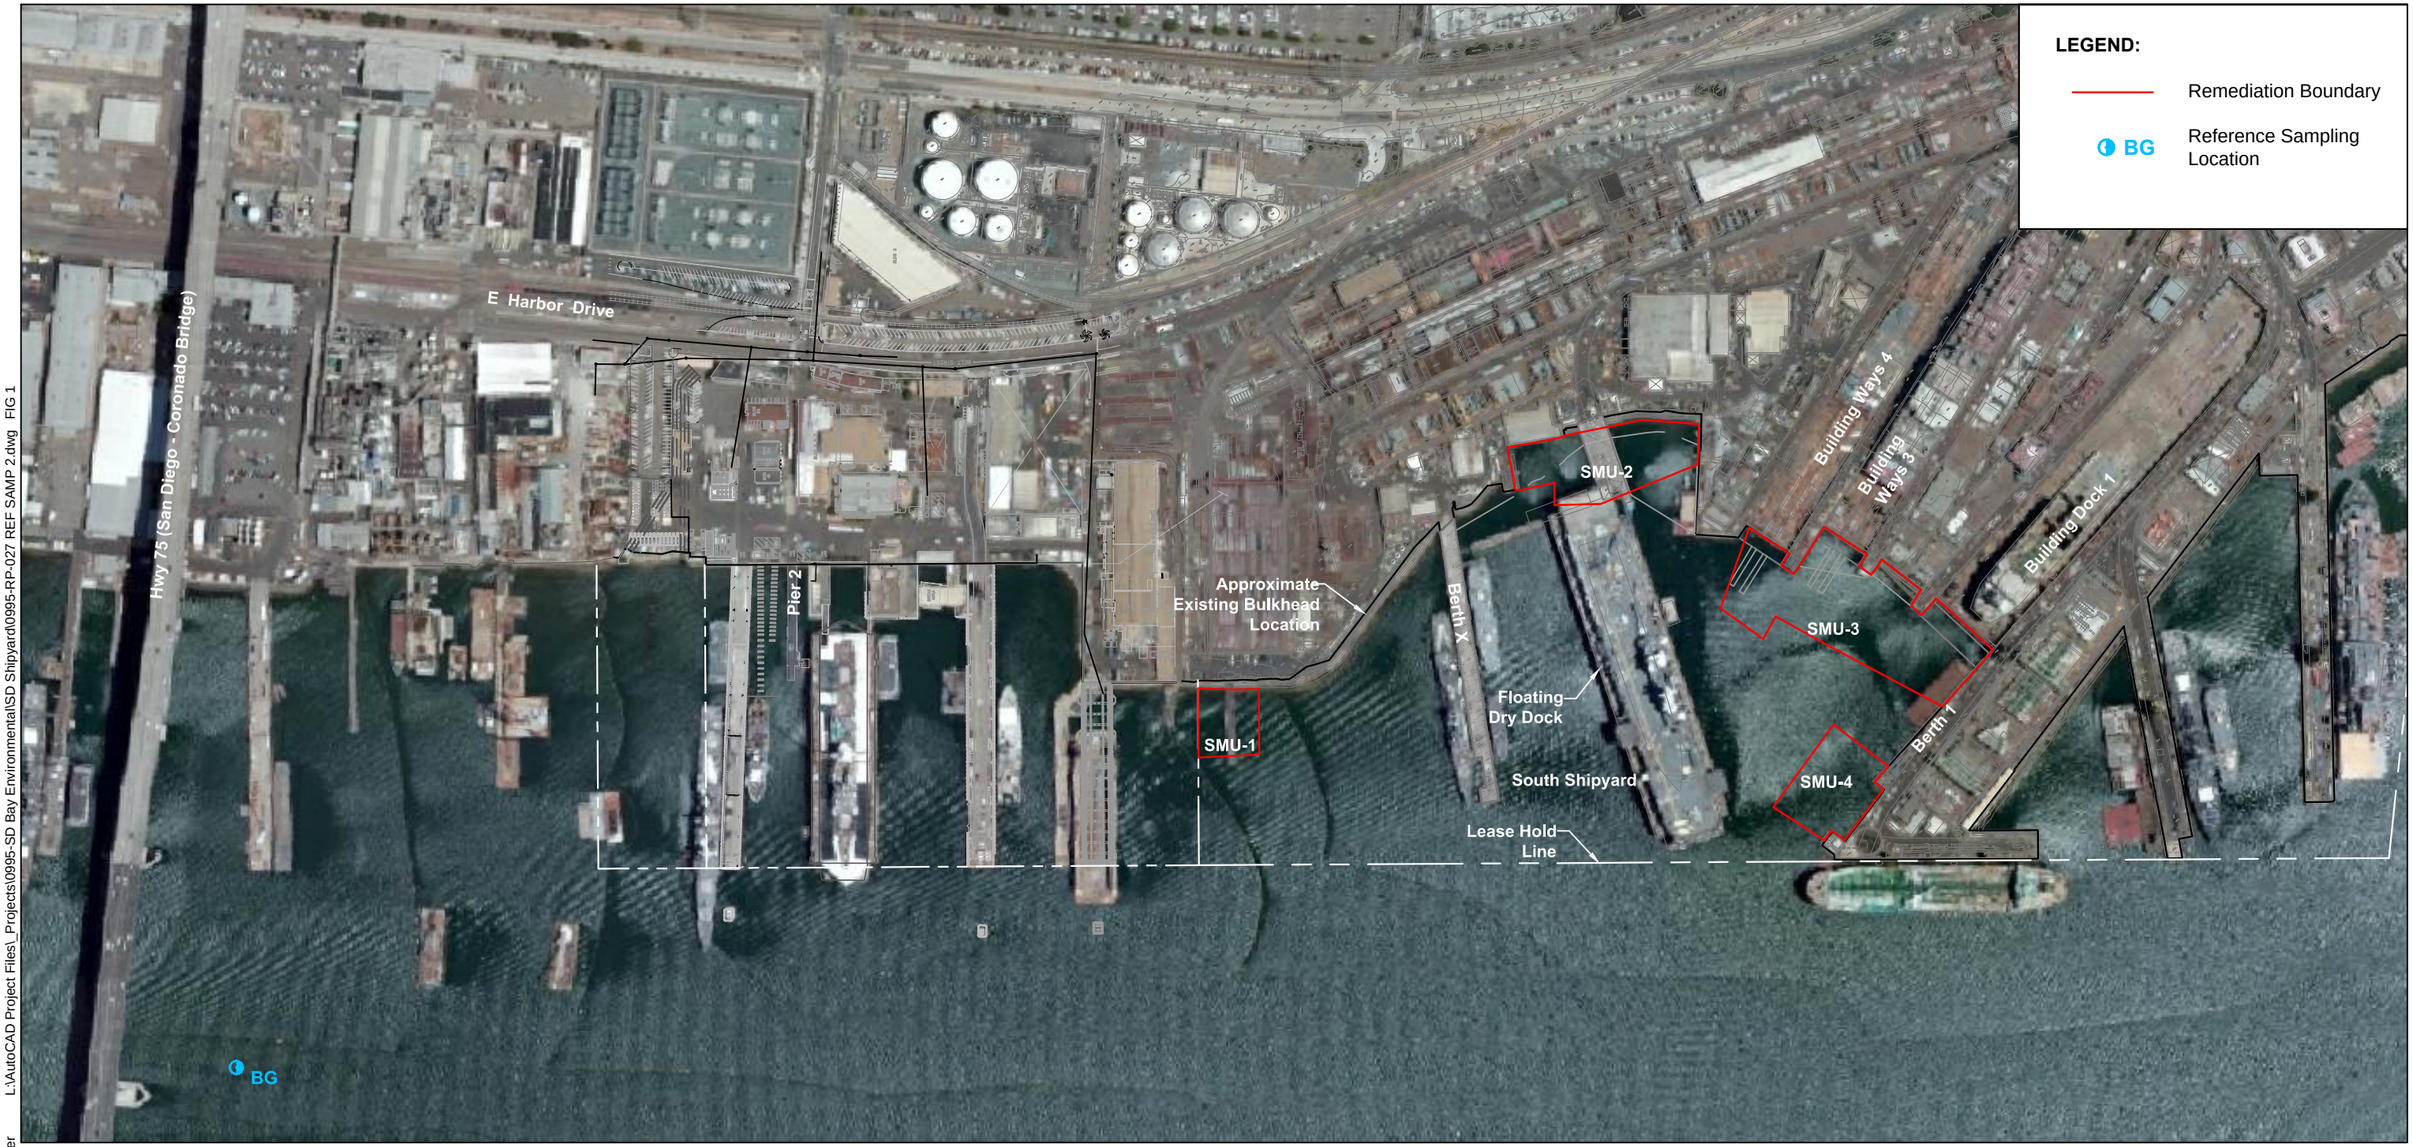

SOURCE: Aerial from ESRI base maps. Upland topography from Digital Mapping Inc., dated September 2009, and supplemented by Environmental Data Solutions survey dated April 13, 2013.
HORIZONTAL DATUM: California State Plane, Zone 6, NAD83, U.S. Feet.

NOTES:
Reference Sampling Location BG
Latitude: 32° 41.4970'
Longitude: 117° 09.0185'

0 350
Scale in Feet

L:\AutoCAD Project Files_Projects\0995-SD Bay Environmental\SD Shipyard\0995-RP-027 REF SAMP 2.dwg FIG 1
Nov 07, 2013 10:04am mpratschner

ANCHOR QEA

Figure 1
Water Quality Reference Sampling Location
San Diego Shipyard Sediment Site - South Shipyard

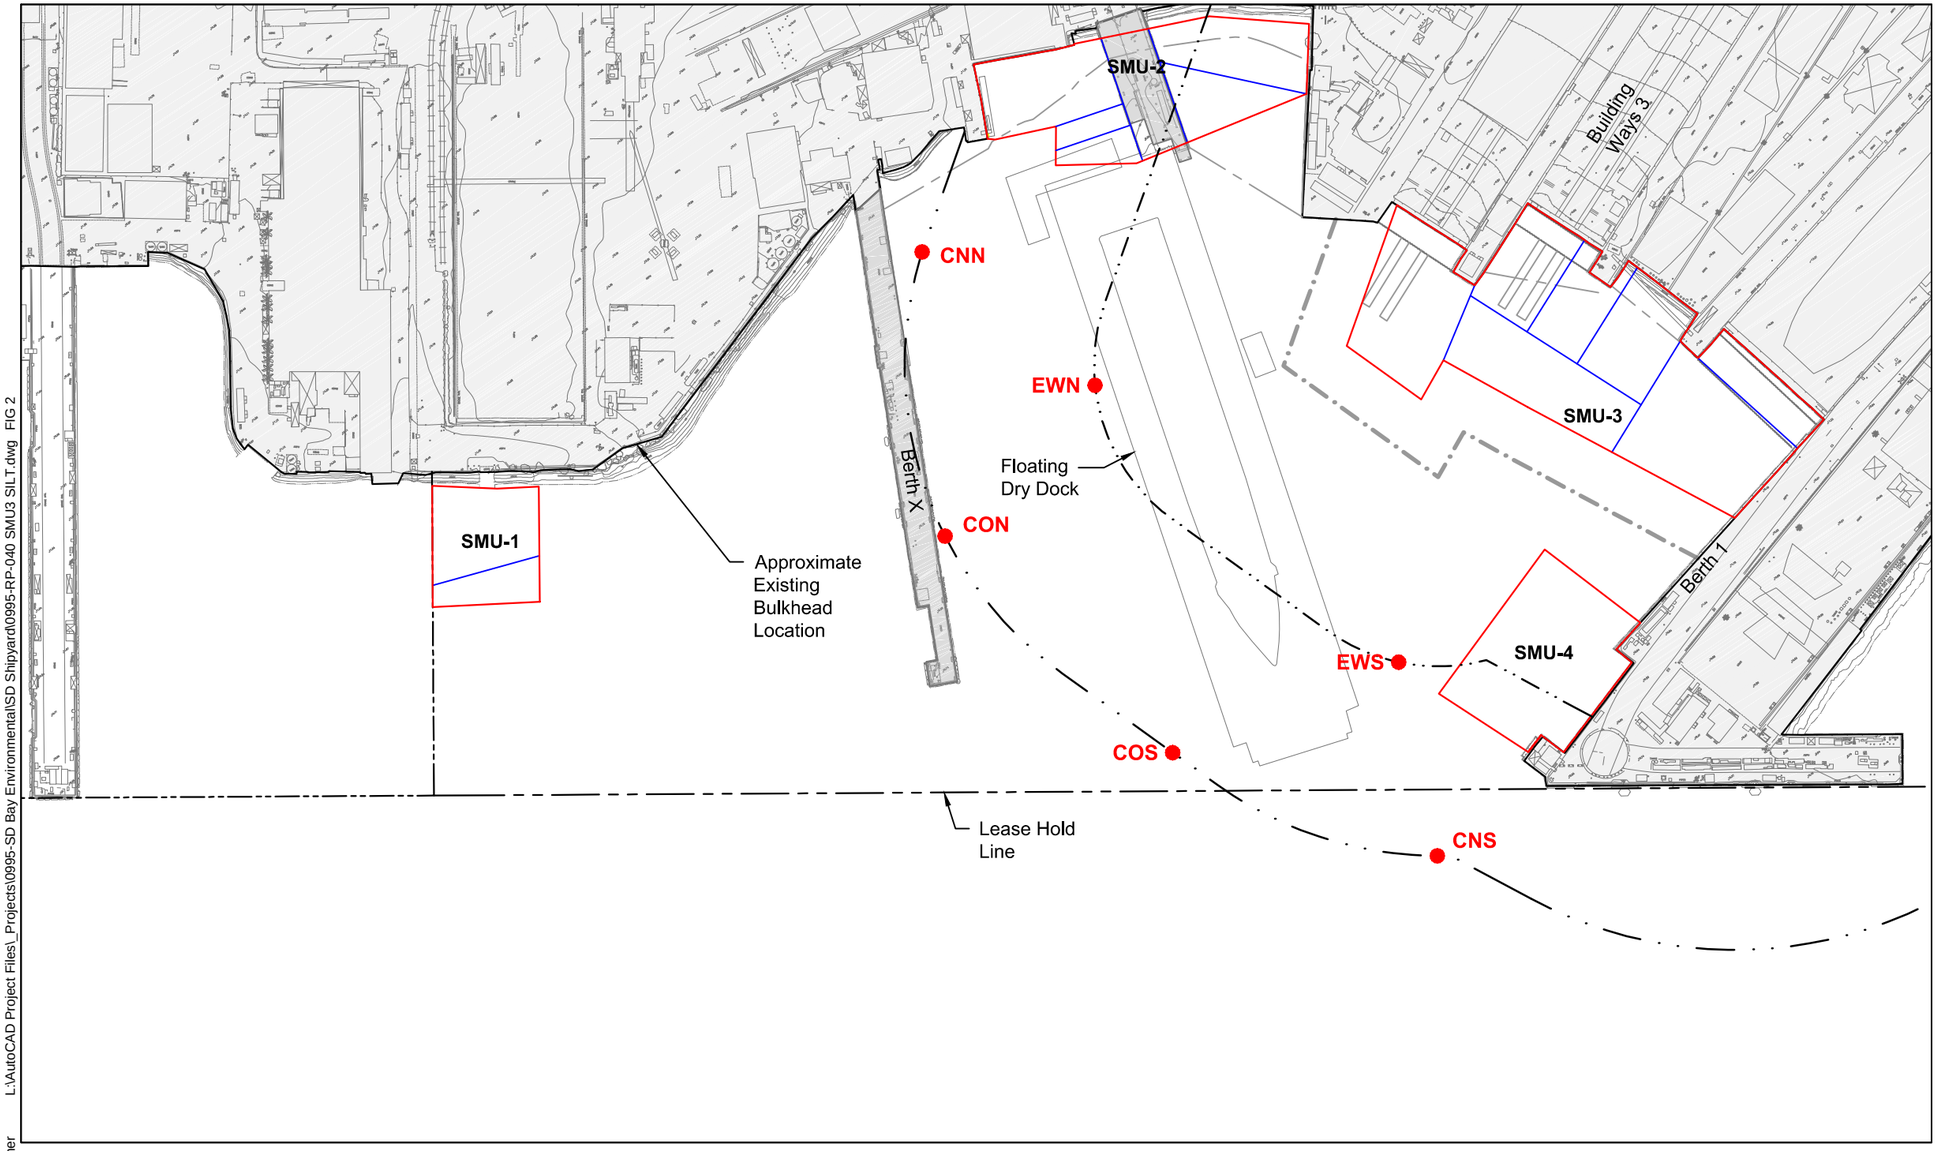

LEGEND:

	Remediation Boundary
	Sub-SMU Boundary
	250 ft from Construction Area
	500 ft from Construction Area
XXX	Sampling Location
	Silt Curtain
EWN	Early Warning North
EWS	Early Warning South
CNN	Compliance Nearshore North
CNS	Compliance Nearshore South
CON	Compliance Offshore North
COS	Compliance Offshore North

NOTE:
Actual locations were positioned in the field relative to the construction area.

SOURCE: Upland topography from Digital Mapping Inc., dated September 2009, and supplemented by Environmental Data Solutions survey dated April 13, 2013.
HORIZONTAL DATUM: California State Plane, Zone 6, NAD83, U.S. Feet.

0 200
Scale in Feet

L:\AutoCAD Project Files_Projects\0995-SD Bay Environmental\SD Shipyard\0995-RP-040 SMU3 SILT.dwg FIG 2
Nov 07, 2013 10:55am mpratschner

ANCHOR QEA

Figure 2
General Layout of Water Quality Sampling Locations for SMU-3
San Diego Shipyard Sediment Site - South Shipyard
